THE I-195 RELOCATION PROJECT

Iway

YOURS. MINE. OURS.

BUILDING DEMOLITION CONTRACTS

- BUILDING DEMO CONTRACT 1 — $245,000 — AS BID
  RI Contract No. 2000-CH-066
- BUILDING DEMO CONTRACT 2 — $737,885 — AS BID
  RI Contract No. 2001-CH-034
- BUILDING DEMO CONTRACT 3 — $1,773,222 — AS BID
  RI Contract No. 2003-CH-021
- BUILDING DEMO CONTRACT 4 — $157,035 — AS BID
  RI Contract No. 2002-CH-007
- BUILDING DEMO CONTRACT 5 — $164,565 — AS BID
  RI Contract No. 2003-CH-022

DEMO CONTRACTS



CONSTRUCTION CONTRACTS

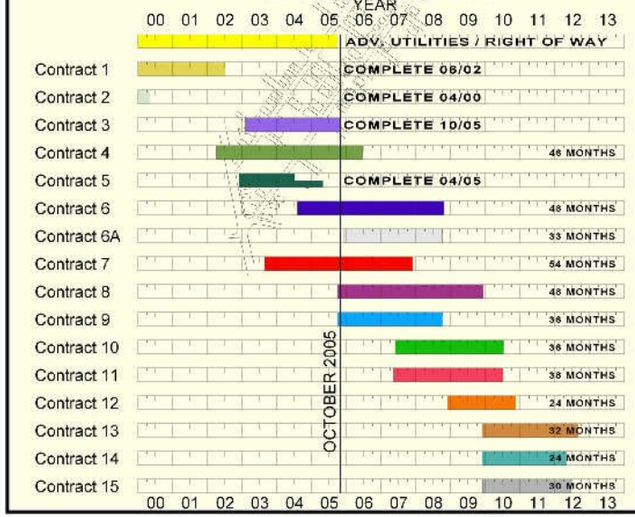

LEGEND

PROPERTY ACQUISITIONS - $45.02 M (TO DATE)
UTILITIES - $30.03 M (TO DATE)

CONTRACT 1 - $4.44 M (AS BID) 1/99
- SOUTH WATER STREET - CRAWFORD STREET BRIDGE TO JAMES STREET
  RI Contract No. 9910

CONTRACT 2 - $0.94 M (AS BID) 11/98
- STORM DRAIN RETROFIT DEMONSTRATION PROJECT
  RI Contract No. 9834

CONTRACT 3 - $5.29 M (AS BID) 11/02
- WEST RIVER WALLS, DYER & EDDY STREETS
- NBC OVERFLOW CULVERTS
  RI Contract No. 2002-CH-060

CONTRACT 4 - $9.59 M (AS BID) 2/02
- POINT STREET OVERPASS
- UTILITY RELOCATIONS
  RI Contract No. 2002-CB-023

CONTRACT 5 - $2.89 M (AS BID) 8/02
- PILE LOAD TEST PROGRAM
- RAMP WN PRELOAD
  RI Contract No. 2002-CH-055

CONTRACT 6 - $63.99 M (AS BID) 7/04
- RAMP NE, WES & WS BRIDGES, I.D. CONSTRUCTION
- ALLENS AVE. BLACKSTONE ST. HENDERSON ST.
  RI Contract No. 2004-CH-030

CONTRACT 6A - $15.50 M (AS BID) 10/05
- PUBLIC, O'CONNELL & OXFORD ST BRIDGES
- I-95 SOUTH - PUBLIC TO THURBERS
  RI Contract No. 2005-CH-190

CONTRACT 7 - $84.55 M (AS BID) 5/03
- RELOCATED INTERSTATE 195
- PROVIDENCE RIVER BRIDGE
  RI Contract No. 2003-CB-011

CONTRACT 8 - $53.99 M (AS BID) 7/05
- RAMPS SE, WN, WP & NP
- FRANKLIN SQ.
  RI Contract No. 2005-CH-051

CONTRACT 9 - $26.11 M (AS BID) 5/05
- PED. BRIDGE / EASTBOUND ON & OFF RAMPS
- INDIA & GANO STREETS / 54" NBC SEWER
  RI Contract No. 2005-CH-052

CONTRACT 10 - $10.52 M **
- I-195 RECONSTRUCTION
- CITY STREETS

CONTRACT 11 - $29.38 M **
- I-95 MAINLINE & ON / OFF RAMPS
- SERVICE ROADS & RAMP PS BRIDGE

CONTRACT 12 - $4.99 M **
- I-95 NORTH - THURBERS TO EDDY
- DUDLEY ST CONNECTOR

CONTRACT 13 - $22.23 M **
- DEMO PROVIDENCE RIVER BRIDGE
- OLD HARBOR CITY STREETS

CONTRACT 14 - $9.39 M **
- DEMO EXISTING INTERCHANGE
- CONSTRUCT CITY STREETS

CONTRACT 15 - $11.32 M **
- DEMO I-195
- CONSTRUCT CITY STREETS

DREDGING - $7.00 M
- PROVIDENCE RIVER

** DENOTES CONTRACT ESTIMATE IN FUTURE DOLLARS BASED ON 2001 ESTIMATE INFLATED AT 2.5% PER YEAR

Maguire Group Inc.
Architects/Engineers/Planners
225 Chapman Street
Providence, Rhode Island 02905

RHODE ISLAND
DEPARTMENT OF TRANSPORTATION

INTERSTATE 195

OCTOBER 18, 2005

200 0 200 400
Scale in Feet

UPDATE 11

IMPROVEMENTS TO INTERSTATE ROUTE 195

PROVIDENCE — RHODE ISLAND

CONSTRUCTION CONTRACT SEQUENCE PLAN
